

West University Place Parks and Recreation Department
Jennie Elizabeth Hughes Park Development
Project Report #5
September 1 – September 14, 2018


Highlights

- The project architect is White Oak Studio, and the general contractor is Landscape Art.
- **Water Feature** – All large boulders and stonework are in place, as well as the plumbing. Contractor has begun working on the base of the feature.
- **Shade Structure** – Brickwork was installed on the steps leading up to the shade structure, the concrete pad, and structure columns. All brickwork associated with the shade structure is complete. Supplies have arrived, and weather permitting, work will begin on the wooden shade structure this week.
- **Landscape** – Nearly all the landscaping is complete on the entire project. The only areas remaining are in high traffic areas around the shade structure and the water feature.
- **Park Pathways** – The last bit of decomposed granite is being placed for the pathway near the water feature. The brickwork on the pathways, paver area, and path edging has been completed.
- **Sidewalks** – The sidewalk running parallel to Pittsburg is completed except for a section near the old driveway.
- **Drinking Fountains** – The plumber be installing the drinking fountain this week pending weather.
- **Site Furnishings** – The site furnishing (benches, bike racks, picnic table) will start to be installed on September 14, and are expected be completed by next week, weather pending.

Water Feature Area



Shade Structure

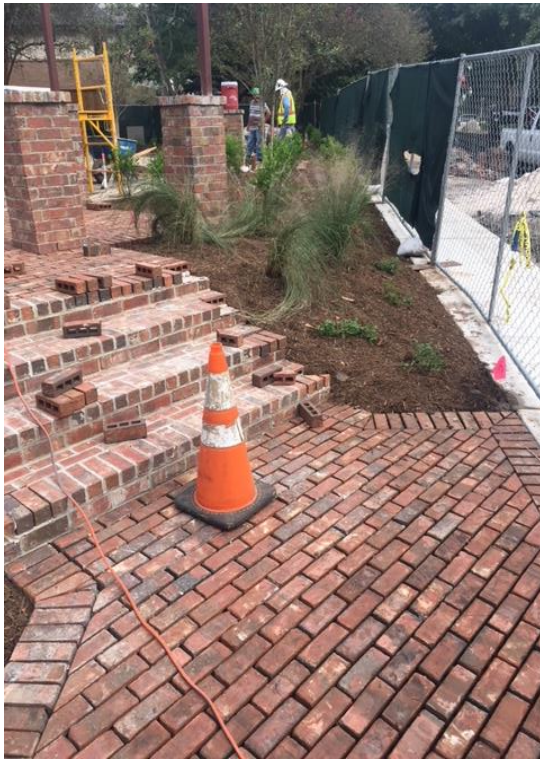




Landscaping





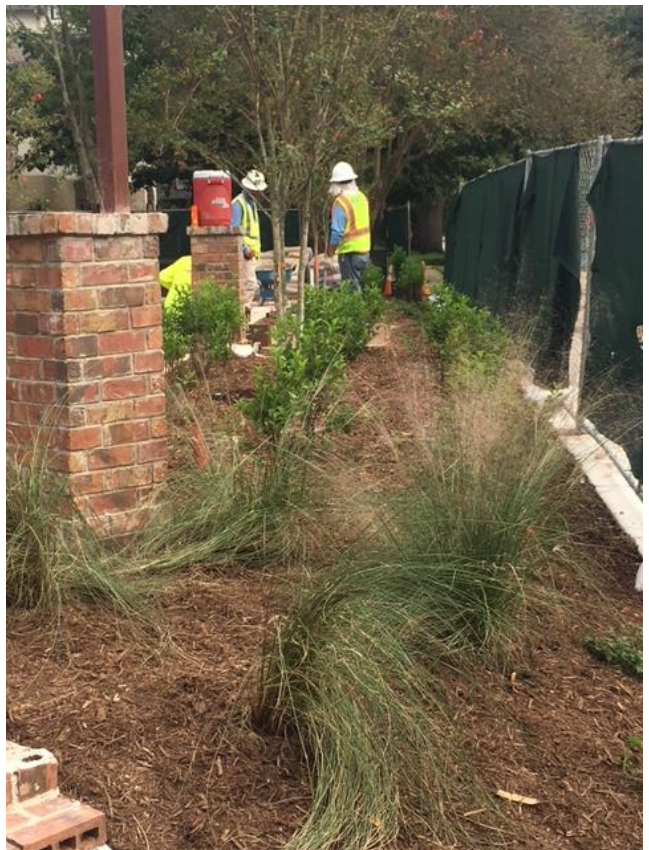

Pathways



