

West University Place Parks and Recreation Department
Jennie Elizabeth Hughes Park Development
Project Report #5
September 15 – October 5, 2018

Highlights

- The project architect is White Oak Studio, and the general contractor is Landscape Art.
- **Miscellaneous** – The speed limit signs for Hughes Park have been installed reducing the speed to 20MPH within 100' of the park.
- **Water Feature** – The rainbow rock aggregate has been added to the bottom on the water feature to form the exposed base of the stream bed. The activation ballast for turning the water feature on has arrived and will be installed by October 5.
- **Shade Structure** – The shade structure is nearing completion. The roof has been constructed and shingles have been laid. The exterior Hardie board is scheduled to be completed by October 5, and painting should begin the week of October 8.
- **Metal Fence** – Currently all fence posts for the perimeter fence are installed. One fence panel has been installed for the exact park sign measurements. The remaining black fence panels are scheduled to be installed by October 6, and the white panels surrounding the front porch structure will be installed next week.
- **Drinking Fountains** – The drinking fountain has been installed inside the park, and the doggie drinking fountain is scheduled to be installed outside the park by October 22.
- **Site Furnishings** – The bike racks, drinking fountain, trash/recycling can, and arched back benches have been installed.
- **Grading & Sod** – Grading has been completed on the open lawn area. The sod for the open lawn area is too wet to cut at the farm, but the contractor is hopeful that the open lawn sod will be installed next week.

Water Feature Area






Shade Structure



Fence

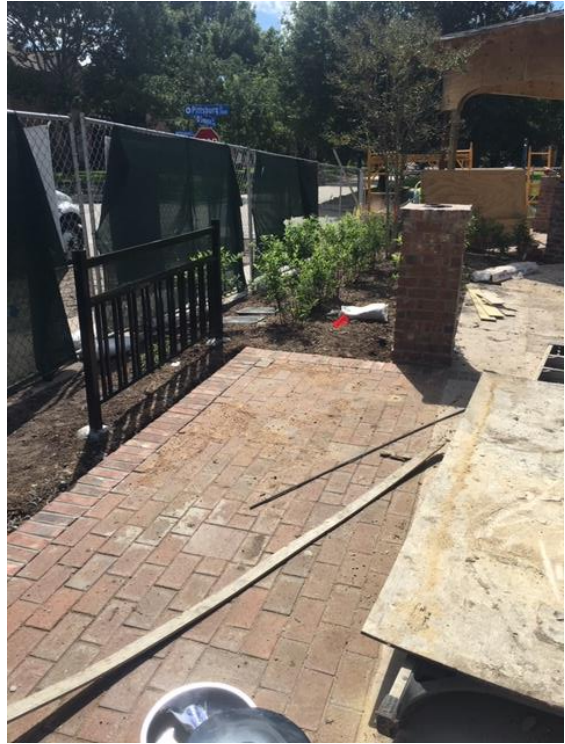

Site Furnishings

