

**West University Place Parks and Recreation Department**  
**Jennie Elizabeth Hughes Park Development**  
**Project Report #1**  
**June 25 – July 13**

**Highlights**

- The project architect is White Oak Studio, and the contractor is Landscape Art.
- Contractor started the project on June 25, a week later than originally scheduled, due to heavy rainfall throughout the week of June 18.
- **Fencing** – Temporary fencing with privacy screening was erected around the project perimeter on June 25. The original wooden fence perimeter fence has been removed and new metal fence posts were installed on June 26 and 27. A concrete mow band was installed at the base of the fence posts along the perimeter fence line. Fence stringer boards are currently being installed, and the fence is scheduled to be completed by July 20.
- **Drainage** - Installation of drainage throughout the property started on June 27. Tied drainage into the storm inlet by breaking out a piece of the sidewalk on Sewanee. Crew backfilled the drainage ditches after the City inspector approved.
- **Water Feature** – Sub-slab layout has been marked out. Work has started on the excavation and forming.
- **Grading** – Rough grading surrounding inlets (within tree drip-line) by hand tool has been completed. Top sod layer and rough grading throughout the property has begun.

**Start of Jennie Elizabeth Hughes Park Development**



**North Property Line**




**West Property Line**



## North Fence Pole Installation



## West Fence Pole Installation

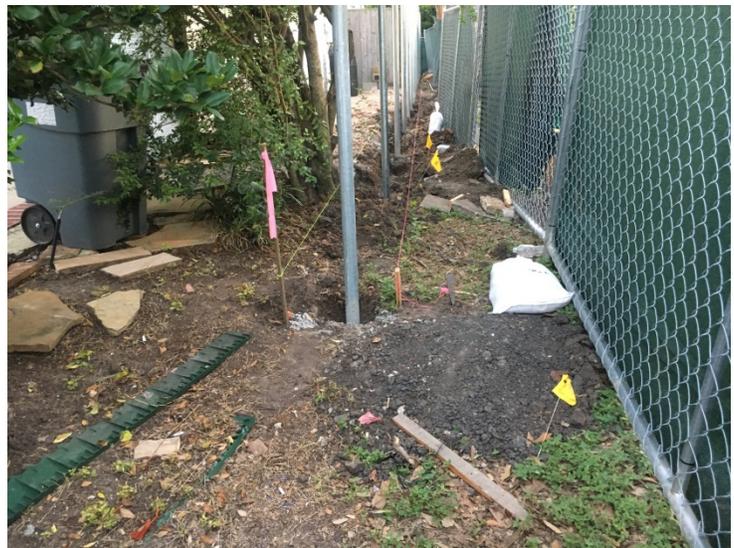

## Drainage



## West Fence Mow Band



## North Fence Mow Band



## Water Feature Sub-Slab Layout



*Project made possible by the generous land and funding bequest from Mr. James Hughes and the Friends of West U Parks Fund, Inc. for their generosity in funding all remaining expenses for this wonderful addition to West U's park system.*
