


**West University Place Parks and Recreation Department**  
**Jennie Elizabeth Hughes Park Development**  
**Project Report #2**  
**July 14 – July 27, 2018**

**Highlights**

- The project architect is White Oak Studio, and the general contractor is Landscape Art.
- **Fencing** – The two sided, 8ft cedar fence with concrete mow band along the north and west sides of the property has been completed.
- **Water Feature** – Plumbing has been set and the concrete slab for the water feature has been poured. Placement of large moss rock boulders around the water feature is underway and is expected to be completed by July 31.
- **Grading** – Crew continues to perform rough grading on the property.
- **Construction Material Testing** – Tolunay-Wong Engineers, Inc., did the testing on the field density/moisture testing on backfill to verify compaction and moisture content compliance, and tested the concrete being used on the pavilion structure and donor paver area. All tests passed.
- **Shade Structure** – Piers for the shade structure foundation have been drilled and approved by the city inspector. The slab for the pavilion foundation was formed and poured on July 25.
- **Donor Paver Area** – The forms were put in place for the Friends of West U Parks paver area and the concrete base was poured on July 25.
- **Irrigation** – Installation of irrigation has begun along the north and west fence lines.
- **Landscape** – Japanese Yew shrubs for the tall border hedge along north and west fence lines arrived on July 26, and are scheduled to be planted by July 27. The Yews are approximately 5ft tall.
- **Electrical** – Conduit has been run for the shade structure.

## Fencing

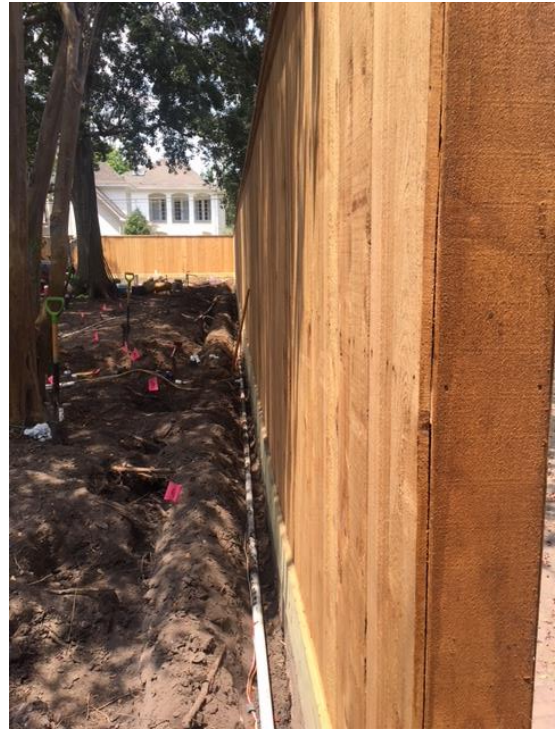



## Water Feature



## Shade Structure





## **Shade Structure**



## **Friends Paver Area and Sidewalk Inside the Park**





## Landscaping

