


Edloe Street Pathway Improvements – Project Report # 2
March 25 – May 5

Highlights

- Project Management Group, LLC (PMG) continued grading along the pathway.
- Removed stumps and fence poles that were left behind after the Harris County Flood Control removed the old fencing and debris. Harris County Flood Control didn't have the equipment to remove these items, therefore PMG had to do the removal to make room for the new fencing.
- Installation of the fencing is currently underway. Adjustments still must be made to the current sections that are installed to check for alignment.
- Installation of the fencing in front of Tiny's parking lot has been installed.
- Relocation of the electrical meter on Tanglely is currently being done.
- Started irrigation connections and lines from Robinhood to Albans.

Photos

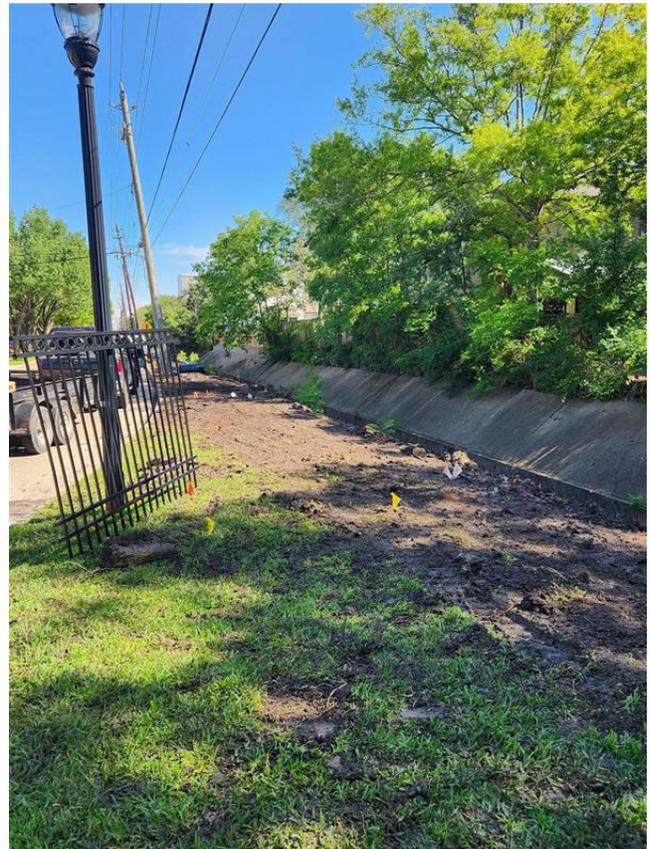

Photos Cont.



Photos Cont.



Photos Cont.

