


Edloe Street Pathway Improvements – Project Report # 5
September 1 – October 31

Highlights

- Worked with PMG on the installation delays of the porous pathway. Allowed the irrigation to run between 6pm – 6am, as more watering was necessary to help the newly installed landscaping survive.
- The pouring of the pathway was completed on September 30. The pet waste dispenser installation was completed, and final landscaping was underway. Staff marked sections of the pathway between Plumb and Georgetown that needed remediation. A substantial completion walkthrough was scheduled for October 17.
- On Wednesday, October 18, Center Point Energy CenterPoint relocated two poles out of the pathway area and the old poles are on their schedule for removal.
- On Monday, October 23, the West University Place City Council, and project staff celebrated the substantial completion of the Edloe Street Pathway.
- The contractor has not completed any more work since the substantial walk through that was held on Tuesday October 17th. The punch list items have been assigned to the contractor, PMG, and they are expected to start the week of November 6 with Piper Whitney on the discolored pathway and addressing other issues.
- Thank you to Friends of West University Parks Fund for garnering donations for the 8 benches along the pathway. See donors below.
 - Alston White
 - Manish Agrawal
 - Jose Lopez
 - Jennifer Starling
 - John Montgomery
 - Jordan Jewett
 - Whitney Walsh
 - Sarah Barrett

Photos

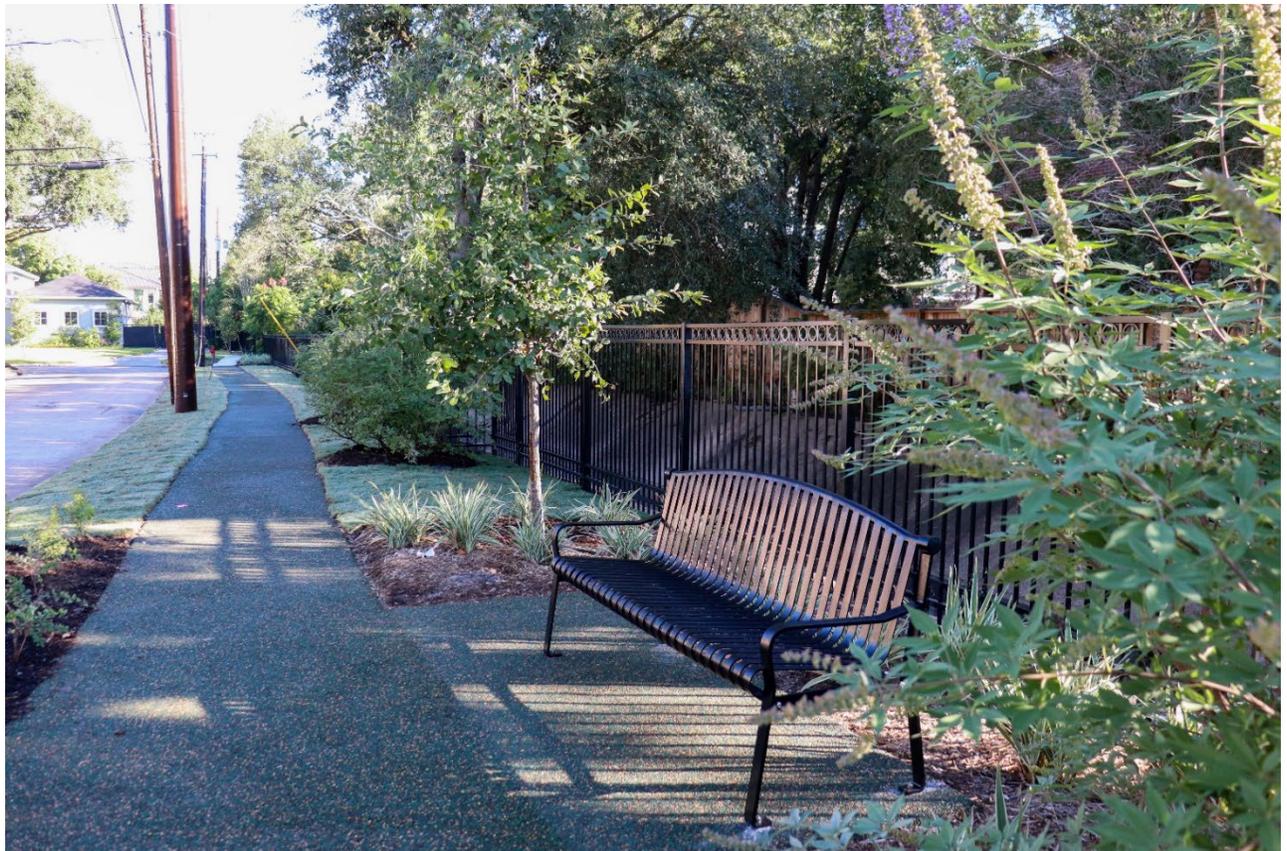

Photos Continued



Photos Continued



Photos Continued



Photos Continued

